

**ICF PACKAGE: Nudura ICF formwork and accessories are our supply. Raft and foundations AS PER THE ARCHITECTURAL DRAWINGS; joist ledgers by the engineer. Floors, stairs, partitions, roof and joinery are drawn as DESIGN ASSUMPTIONS for coordination - check by the relevant professional.**

**FOR APPROVAL - NOT FOR CONSTRUCTION**

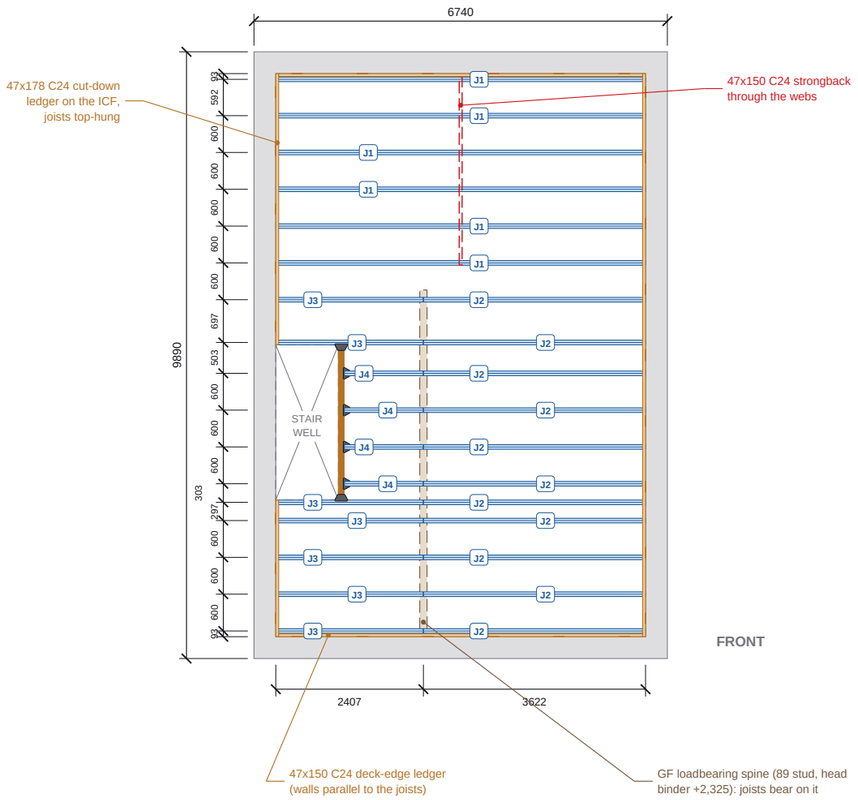


## FIRST FLOOR JOIST LAYOUT

Scale 1:100 @ A3 | Plan on the FF joists, deck omitted

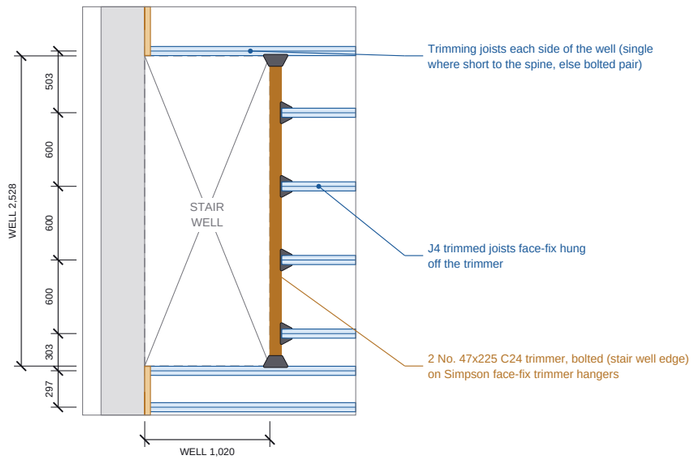


## STAIR WELL FRAMING U1 - ENLARGED

Scale 1:50

Metal-web joist 253 (type J)
C24 ledger
GF loadbearing spine (below)
Strongback
Connector / hanger / clip
ICF walls (FF outline)

0 1 2 3 4 5m

Do not scale. All dimensions in mm. Check all dimensions on site.

## FIRST FLOOR SCHEDULES

### JOIST SCHEDULE (253 DEEP, @600)

| Type | O/A | Bottom | U1 | Total |
|---|---|---|---|---|
| J1 | 6,023 | 5,929 | 6 | 6 |
| J2 | 3,617 | 3,570 | 11 | 11 |
| J3 | 2,402 | 2,355 | 7 | 7 |
| J4 | 1,288 | 1,288 | 4 | 4 |
| | **Total** | | **28** | **28** |

O/A = top flange overall length; Bottom = bottom flange length. Includes 0 No. in doubled trimming pairs. Profiles on ES26-020-POW-FL-02.

### LEDGERS, STRONGBACKS, TRIMMERS (C24)

| Item | Length | Qty |
|---|---|---|
| 2 No. 47x225 trimmer, bolted (stair well) | 2,528 | 1 |
| 47x150 deck-edge ledger | 5,935 | 2 |
| 47x150 strongback | 3,065 | 1 |
| 47x178 ledger cut-down ledger | 9,179 | 1 |
| 47x178 ledger cut-down ledger | 4,419 | 1 |
| 47x178 ledger cut-down ledger | 2,226 | 1 |

### METALWORK AND DECK

| Item | Qty |
|---|---|
| 22 Egger Protect P5 T&G board | 49 |
| Face-fix joist hanger | 4 |
| Face-fix trimmer hanger | 2 |
| Strong-Tie ICFVL-CW + ICFLC connector | 29 |
| Top-chord restraint clip (galv) | 30 |

### NOTES

1. First floor (DESIGN ASSUMPTION for coordination): 253 deep metal-web joists (72 x 47 C24 flanges, Posi-Joist / Easi-Joist equivalent) at 600 c/c spanning x, from the ICF walls onto the GF loadbearing spine (GF spine G7: 89 timber stud, head binder at +2,325); 6 No. clear-span joists wall to wall past the end of the spine.
2. TOP-HUNG at the ICF: the top flange runs over a 47 x 178 C24 ledger (47 x 225 ripped down) and stops 3 short of the ICF face; the bottom flange stops 3 short of the ledger. Galv restraint clip at every ledger bearing. At the spine the joists bear on the head binder, butted over its centre and fixed to it.
3. Ledgers fixed to the ICF with cast-in Simpson Strong-Tie ICFVL-CW + ICFLC connectors - ledgers and their fixings by the engineer. Top of ledger +2,531, top of joists +2,578, FF FFL +2,600 above GF FFL.
4. Deck: 22 Egger Protect P5 T&G, glued and screwed to every joist. 47 x 150 C24 deck-edge ledgers on the walls parallel to the joists. 47 x 150 C24 strongback through the webs where shown.
5. Stair well: trimming joists each side - SINGLE where the piece carrying the trimmer spans <= 3,200 to the GF spine, otherwise doubled (bolted pair); 2 No. 47 x 225 C24 trimmer bolted on face-fix trimmer hangers, each hanger at a joist WEB NODE / web stiffener (point load - joist designer to confirm); trimmed joists face-fix hung. Joist supplier / engineer to design and confirm joist depth, spacing, bracing and bearings (clear spans are long for 253 joists - design assumption, joist supplier to confirm).
6. Powys (detached), plot 14, building B05. Datum 0 = GF FFL. Architect: Beech Developments - BD0154-POW rev A (JHG 26/10/26).

### REVISIONS

| REV | DATE | DESCRIPTION |
|---|---|---|
| P01 | 29.10.26 | Approval issue |

Nudura™ BuildEase

| CLIENT | PROJECT |
|---|---|
| Beech Developments (NW) Ltd | Maes Y Felin, Glan Conwy - Powys |

DRAWING TITLE

**POWYS - FIRST FLOOR LAYOUT**

Metal-web joists, ledgers, GF spine bearing, stair well trimming

| SCALE | SIZE | DATE |
|---|---|---|
| AS SHOWN | A3 | 29.10.26 |
| DRAWN | CHECKED | APPROVED |
| TS | | |

| STATUS | DRAWING No. | REV |
|---|---|---|
| FOR APPROVAL | ES26-020-POW-FL-01 | P01 |
