Delivery 1 - Load 1 of 1 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 165 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

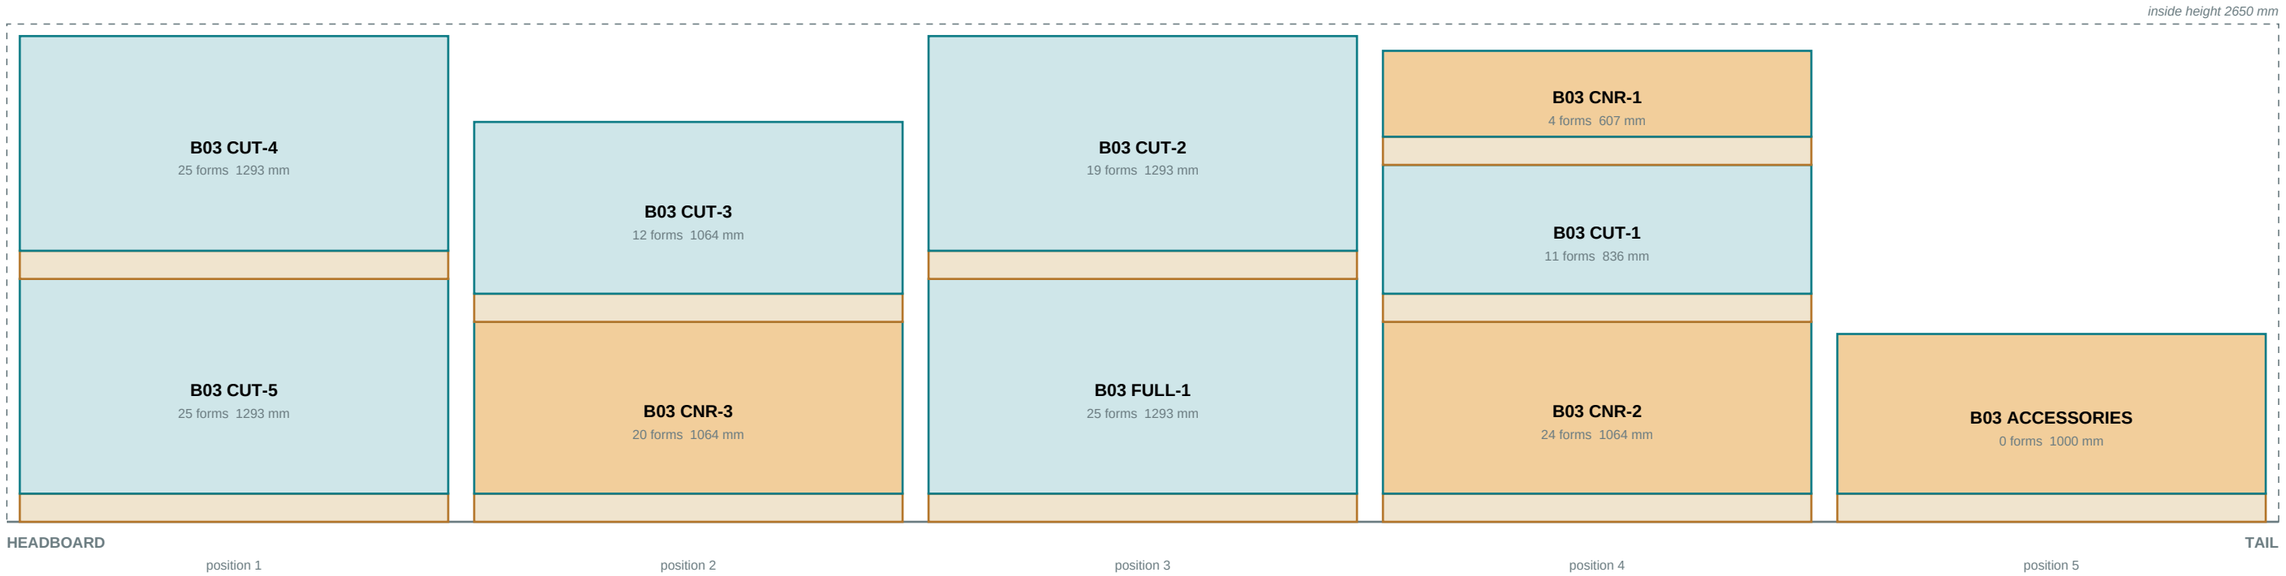

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. B03 ACCESSORIES 6in XR35 accessoriess 0 forms courses -
2. B03 CNR-1 6in XR35 corners 4 forms courses FB course 1
3. B03 CUT-1 6in XR35 straights 11 forms courses FB course 1
4. B03 CNR-2 6in XR35 corners 24 forms courses L1 courses 1-6
5. B03 CUT-2 6in XR35 straights 19 forms courses L1 courses 1-6
6. B03 FULL-1 6in XR35 straights 25 forms courses L1 courses 1-6
7. B03 CUT-3 6in XR35 straights 12 forms courses L1 courses 3-6
8. B03 CNR-3 6in XR35 corners 20 forms courses L2 courses 1-5
9. B03 CUT-4 6in XR35 straights 25 forms courses L2 courses 1-5
10. B03 CUT-5 6in XR35 straights 25 forms courses L2 courses 4-5

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-020 Maes Y Felin - B03 plots 12	FORMS	165
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2586 mm
