Delivery 1 - Load 1 of 2 - 18 t rigid

6 pallets in 3 of 3 floor positions | 86 forms | tallest column 2586 mm of 2650 mm inside height

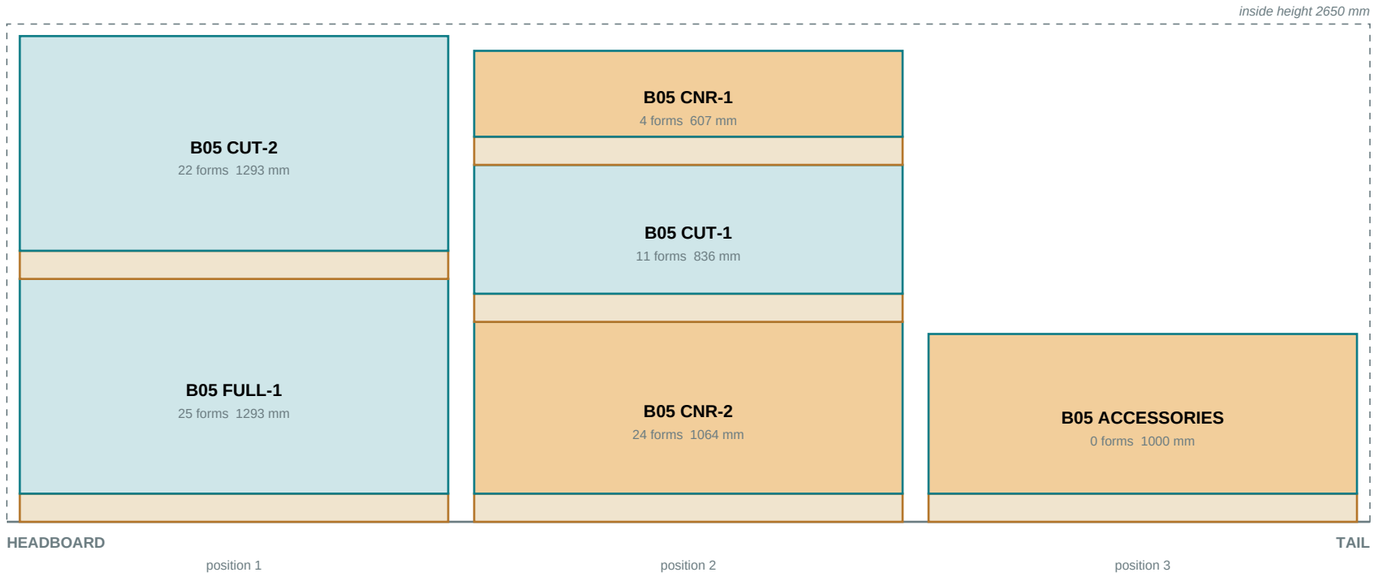

Unload order - 5 of 5 pallets come off out of build order, the price of stacking tallest forward

1. B05 ACCESSORIES 6in XR35 accessoriess 0 forms courses -
2. B05 CNR-1 6in XR35 corners 4 forms courses FB course 1
3. B05 CUT-1 6in XR35 straights 11 forms courses FB course 1
4. B05 CNR-2 6in XR35 corners 24 forms courses L1 courses 1-6
5. B05 CUT-2 6in XR35 straights 22 forms courses L1 courses 1-6
6. B05 FULL-1 6in XR35 straights 25 forms courses L1 courses 1-6

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-020 Maes Y Felin - B05 plots 14	FORMS	86
VEHICLE	18 t rigid	POSITIONS	3 of 3
PALLETS	6	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - 18 t rigid

6 pallets in 3 of 3 floor positions | 116 forms | tallest column 2586 mm of 2650 mm inside height

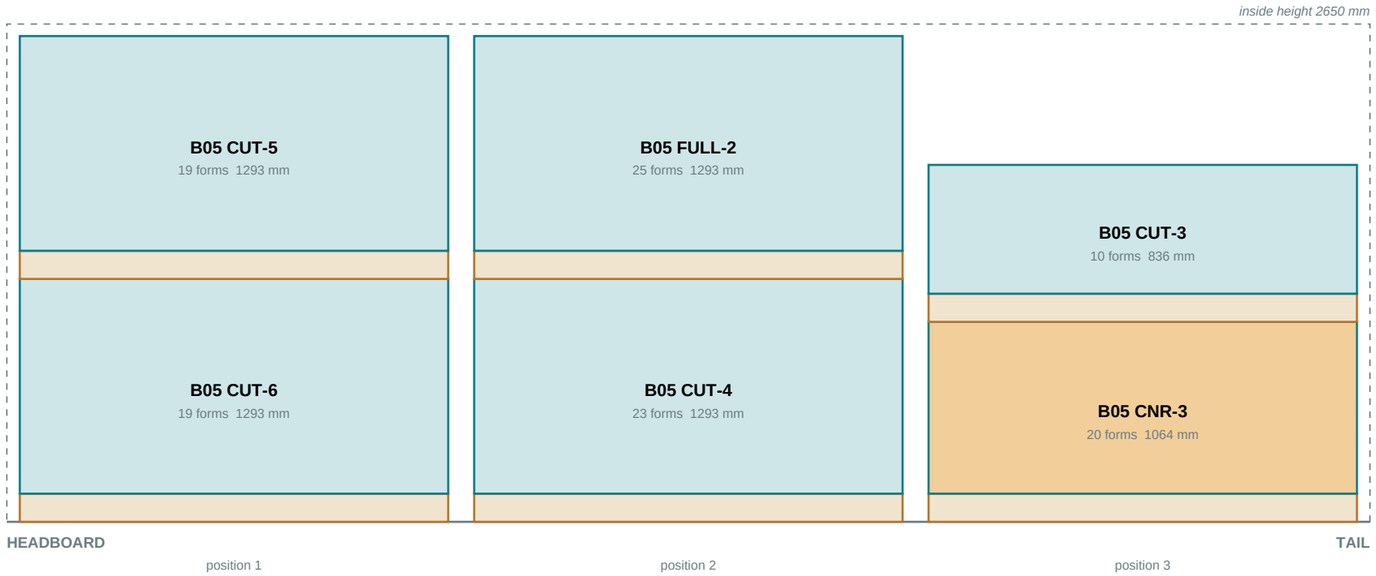

Unload order - 5 of 5 pallets come off out of build order, the price of stacking tallest forward

1. B05 CUT-3 6in XR35 straights 10 forms courses L1 courses 4-6
2. B05 CNR-3 6in XR35 corners 20 forms courses L2 courses 1-5
3. B05 FULL-2 6in XR35 straights 25 forms courses L2 courses 1-6
4. B05 CUT-4 6in XR35 straights 23 forms courses L2 courses 1, 2, 3, 4, 6, 7, 8, 11, 12
5. B05 CUT-5 6in XR35 straights 19 forms courses L2 courses 3, 4, 5, 6, 7, 9, 10
6. B05 CUT-6 6in XR35 straights 19 forms courses L2 courses 7-12

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-020 Maes Y Felin - B05 plots 14	FORMS	116
VEHICLE	18 t rigid	POSITIONS	3 of 3
PALLETS	6	TALLEST	2586 mm
