Delivery 1 - Load 1 of 2 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 163 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

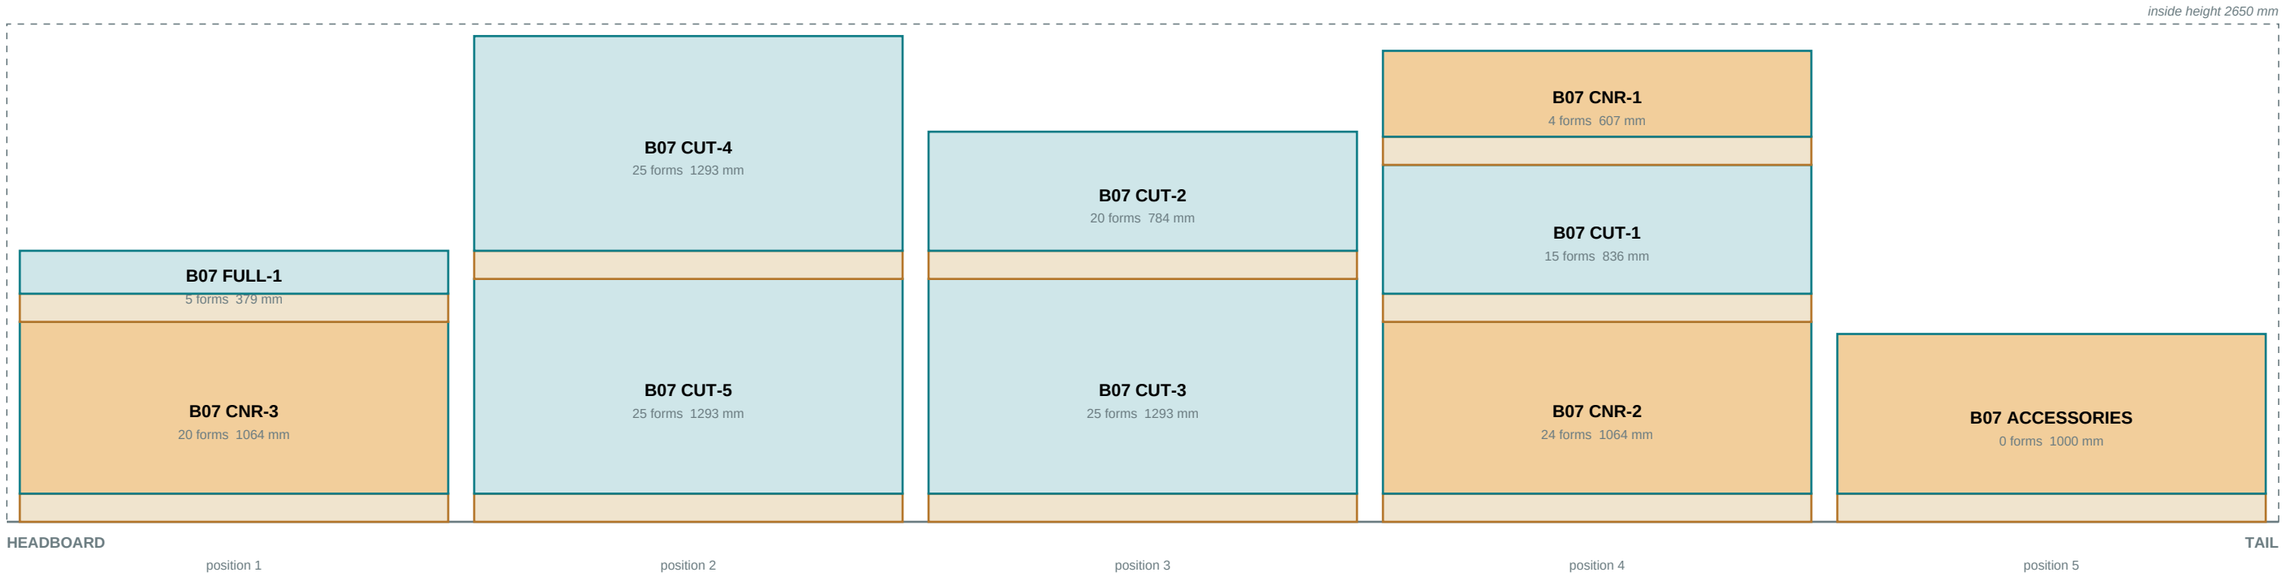

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. B07 ACCESSORIES 6in XR35 accessoriess 0 forms courses -
2. B07 CNR-1 6in XR35 corners 4 forms courses FB course 1
3. B07 CUT-1 6in XR35 straights 15 forms courses FB course 1
4. B07 CNR-2 6in XR35 corners 24 forms courses L1 courses 1-6
5. B07 CUT-2 6in Std straights 20 forms courses L1 courses 1-6
6. B07 CUT-3 6in XR35 straights 25 forms courses L1 courses 1-6
7. B07 CUT-4 6in XR35 straights 25 forms courses L1 courses 2-5
8. B07 CUT-5 6in XR35 straights 25 forms courses L1 courses 4-6
9. B07 FULL-1 6in XR35 straights 5 forms courses L1 course 6
10. B07 CNR-3 6in XR35 corners 20 forms courses L2 courses 1-5

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-020 Maes Y Felin - B07 plots 16, 17	FORMS	163
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - 18 t rigid

5 pallets in 3 of 3 floor positions | 127 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

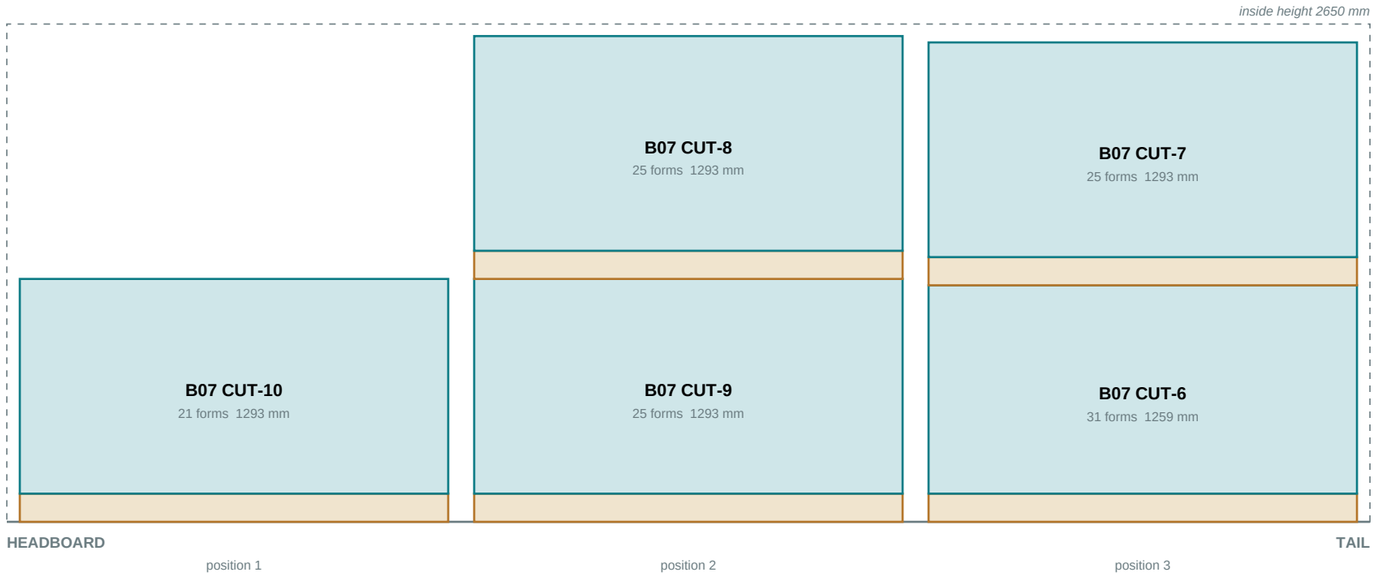

Unload order - 4 of 4 pallets come off out of build order, the price of stacking tallest forward

1. B07 CUT-7 6in XR35 straights 25 forms courses L2 courses 1, 2, 3, 5, 7, 9
2. B07 CUT-6 6in Std straights 31 forms courses L2 courses 1-12
3. B07 CUT-8 6in XR35 straights 25 forms courses L2 courses 3-7
4. B07 CUT-9 6in XR35 straights 25 forms courses L2 courses 5, 6, 7, 9, 10
5. B07 CUT-10 6in XR35 straights 21 forms courses L2 courses 7-11

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-020 Maes Y Felin - B07 plots 16, 17	FORMS	127
VEHICLE	18 t rigid	POSITIONS	3 of 3
PALLETS	5	TALLEST	2586 mm
